



TDOT
Department of
Transportation

Nolensville Pike / State Route 11 Widening Newsletter


September 2026

Project Description:

The current project on Nolensville Pike improves widens State Route 11 from a primarily two-lane route to a five-lane roadway and includes dedicated turn lanes, bike lanes, and sidewalks. It stretches from near SR 254 (Old Hickory Boulevard) to north of Mill Creek in southern Davidson County. The proposed improvements are intended to address congestion, improve safety, and accommodate growth in this rapidly developing area.

Traffic Note:

- Sugar Valley Drive at Nolensville Pike (SR 11) is closed until mid-October. Local traffic is able to access Sugar Valley Drive from Sunnywood Drive. See the suggested detour below:

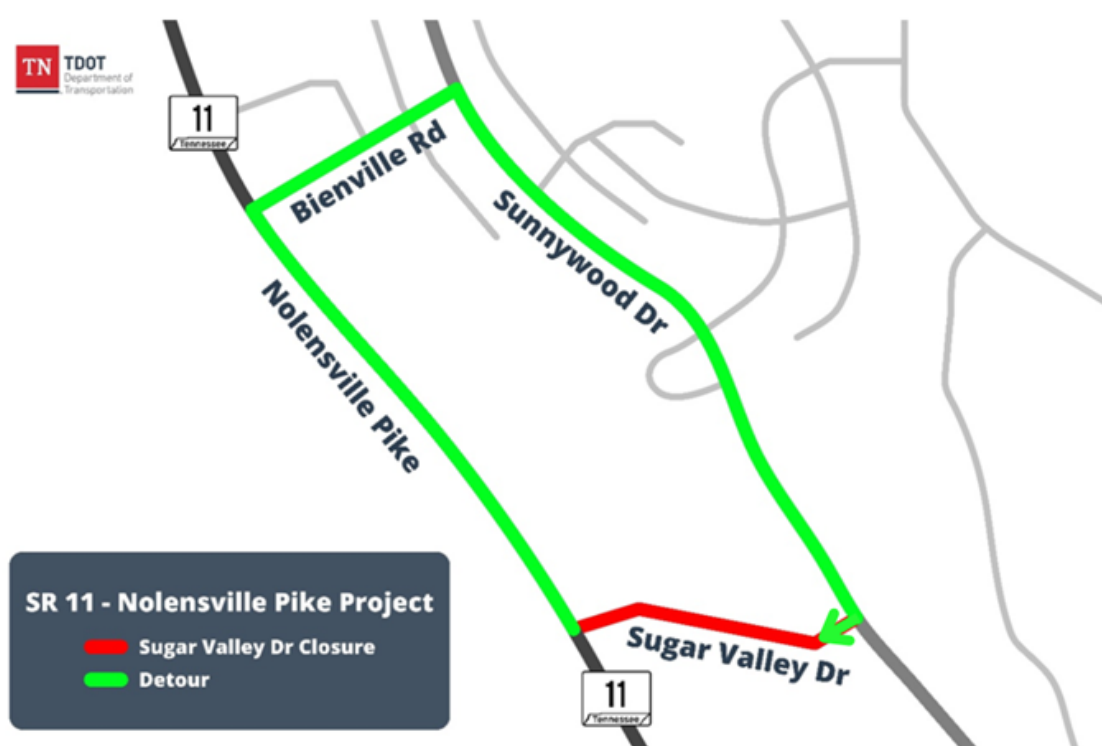

1. Completed Work:

1. Installed buried utilities, including water and gas lines.
2. Placed storm drainage.
3. Completed water line installation from Hills Chapel Road to Bradford Hills Drive.





Water line installation.

- Finished retaining wall 2 at the intersection of Kinhawk Drive and Nolensville Pike.
- Poured the remaining soldier pile retaining wall panels south of Kinhawk Drive.



Retaining wall 2 completion.

- Finished placing the mainline arch culvert on the north end of the project.



Mainline arch culvert placement.

- Sugar Valley Closure: Finished buried gas line utilities.

1. Active Work:

1. Installing the remaining gas line from Bradford Hills Drive to Celebration Way.
2. Installing water line from Shadow Glen Drive to the end of the project.
3. Placing storm drainage throughout the project.
4. Completing the stream five relocation between Shadow Glen Drive and

new channel, stabilization, and plantings.



Stream 5 relocation.

- Installing the remaining utility poles and power lines from Barnes Road to the end of the project (Old Hickory Blvd).



Power relocations.

- Installing base stone and underdrain from the beginning of the project to Sugar Valley Drive (East Side/Phase 2).



Base stone installation.

- Sugar Valley Closure: Placement of the remaining box culvert installation.



Box culvert placement.

- **Upcoming Work:**
 - Continuing installation of water, sewer, and gas lines.
 - Continuing storm drainage placement.
 - Install curb and gutter and sidewalk after base stone and underdrain placement from the beginning of the project to Sugar Valley Drive (East Side/Phase 2).
 - Finish communication relocations when power relocation is finished from Barnes Road to the end of the project.

Project Contacts

- **Erin Zeigler**
TDOT Region 3 Communications Officer
Phone: 629.277.2458
Email: Erin.Zeigler@tn.gov
- **Greg Woerdeman, PE**
TDOT Region 3 District Operations Supervisor (Construction)
Phone: 615.350.4461
Email: Greg.Woerdeman@tn.gov

[Manage](#) your preferences | [Opt Out](#) using TrueRemove™

Got this as a forward? [Sign up](#) to receive our future emails.

View this email [online](#).

505 Deadrick Street | Nashville, TN 37243 US

This email was sent to .

To continue receiving our emails, add us to your address book.

emma®
