



# HISTORIC DEVELOPMENT GRANT COMPLIANCE WEBINAR

Grants Management

**COURTHOUSE ROUND**

February 6, 2026

# Congratulations!

11 New Grantees



Chester County



Dickson County



Giles County



Lauderdale County



Lawrence County



Maury County



Morgan County



Pickett County



Polk County



Scott County



Weakley County



# Agenda

- Overview
- Contracts
- Compliance
- Procurement
- Financial Requirements
- Reporting
- Monitoring
- File Retention
- Closeout Documents
- Other requirements

# About the Program



In April 2021, the Tennessee General Assembly developed the Historic Development Grant Program and allocated \$4.8 million to renovate and preserve the State's historic buildings. The legislators recognized that historic buildings and their preservation expand the state's economy, create new employment opportunities, revitalize and renew communities, create an environment for investment, and promote tourism and rural economic development.



For the 2025/2026 Budget year, the Tennessee General Assembly allocated funding to provide grants to eligible historic courthouses across the state. Counties with eligible courthouses will be notified by TNECD staff.

# Grant Compliance

The **Grants Administration Website** contains all the information you are required to submit to get your contract started and to manage your project.

- Grant Payment Setup Form, W9 & Direct Deposit Form  
*(You have already done these)*
- Audit & Title VI *(Must be submitted prior to requesting reimbursement)*
- Contract Scope Change Request
- Reimbursement Instructions
- Accrued Liability Instructions
- Cumulative Adjustment Instructions
- Budget Revision Form

# Grant Administration Requirements

- Grants awarded for \$75,000 or more are required to work with a third-party grant administrator
- The grant administrator must work for or be an employee of an established grant administration entity that has **3 or more years** of experience managing state or federal grants.
- If your grant administrator listed in the application is not with a professional grant administration firm, please provide a resume and job description for approval
- Grant administration cannot exceed 5% of the original grant award
- Example overview of qualifying admin costs ([Found Here](#))

# Audit & Title VI

## Financial Audit (Updated Annually)

### Items Needed for Compliance

- Most Recent Audit
  - If you are a City or County, you do not need to upload an audit as long as it is filed with the Comptroller's Office.
  - If you are not audited, we need your Form 990 if you are a nonprofit or an annual report that contains audited financials.
- Corrective Action Plan
  - If your organization had audit findings, upload a copy of your organization's Corrective Action Plan if it is not a part of the audit document.

## Title VI Compliance (Updated Every Three Years)

### Items needed for Compliance

- A copy of your organizations Title VI Non-Discrimination Policy.
- Title VI Survey
- Title VI Training Certificate
  - The survey, training and quiz can be found on the submission website.

### *Things to Note*

- These items must be submitted prior to requesting reimbursement
- If you have already submitted for another TNECD program this does not have to be submitted again.

# Contracts

 <b>GOVERNMENTAL GRANT CONTRACT</b> <small>(cost reimbursement grant contract with a federal or Tennessee local governmental entity or their agents and instrumentalities)</small>			
<b>Begin Date</b>	<b>End Date</b>	<b>Agency Tracking #</b>	<b>Edison ID</b>
You cannot incur expenses before this date	You cannot incur expenses after this date	The number of the program internally (budget)	The number for this contract, also referred to as a "PO" number
<b>Grantee Legal Entity Name</b>			<b>Edison Vendor ID</b>
Legal Name of your organization, including a dba, if applicable			The number associated with your entity
<b>Subrecipient or Contractor</b>		<b>CFDA #</b>	
<input checked="" type="checkbox"/> Subrecipient <input type="checkbox"/> Contractor		<b>Grantee's fiscal year end</b> This is the end of your fiscal year per your application and <del>pregrant</del>	

Section	Description
A	Scope of Services and Deliverables
B	Term of Contract
C	Payment and Conditions
D	Standard Terms and Conditions
E	Special Terms and Conditions
Attach. A	Detailed Scope of Services
Attach. 2	Budget

# Contracts

- When you receive the draft contract verify the information before returning it signed
- Do NOT start work until you have an executed contract - We can only reimburse for expenses during the approved contract period!
- Contracts outline eligible timeline, activities and budget
- Contracts are active for three years.

# Contracts- Scope of Work

A.1. The Grantee shall provide the scope of services and deliverables (“Scope”) as required, described, and detailed in this Grant Contract.

A.2. The Grantee shall utilize funds to rehabilitate the historic building as described in Attachment A – “Historic Preservation Certification Application Part 2 – Description of Rehabilitation”. \*\*\*

- Part 2 Conditions from Tennessee Historical Commission are attached to your contract and include instructions on how to gain approval prior to beginning your project.
  - Conditions are specific for each project and are an addendum to Part 2 that has been submitted and reviewed by the Tennessee Historical Commission.
  - Any change in the scope of work must be reviewed, and approved, by the Tennessee Historical Commission prior to work being undertaken in order to ensure the rehabilitation will meet the overall historic character of a building has been retained. As such, this may include work not described in the Part 2 but performed during the grant period.

*\*\*\*Lawrence, Morgan, Scott and Weakley County’s Courthouse must be listed on the National Register of Historic Places prior to completion of the grant. This process can happen concurrently while working on this grant. The county will need to reach out to the Tennessee Historical Commission if they haven’t already to begin this process.*

# Contracts- Scope of Work

A.3. The Grantee shall submit photos and documentation to show completion of scope of work or, as required, a "Historic Preservation Certification Application Part 3 - Request for Certification of Completed Work" for review and approval by the State Historic Preservation Office prior to close-out of this grant and reimbursement under Section C.3. of this Grant Contract.

A.4. The Grantee shall complete the work in compliance with the Secretary of the Interior's Standards for, 36 CFR 67. Information on the Standards is available from the National Park Service (<https://www.nps.gov/tps/standards/rehabilitation.htm> ).

A.5 The Grantee shall not sell, transfer, or otherwise dispose of the property described in Section A.2 during the Terms of this Grant Contract.

# Procurement

- Procurement must be **competitive and transparent**
- Follow local procurement procedures and keep good documentation of the process and results
- Procurement of professional services should not be based on price but on meeting your qualifications

# Procurement of Professional Services

Public advertising is not required, however you must follow [TCA12-4-107](#), Contracts for Professional Services

The steps below are used for the procurement of grant administration, engineering/architectural services, project management, third-party training and design services. Contracts should be awarded based on qualifications, **not price alone**

Step	Activity	Documentation
1	Prior to the engagement of any professional services, a written request for statements of qualifications must be sent to at least three firms that offer the type of service the community wishes to procure	Copies of letters or emails sent
2	Once statements of qualifications are received back from the firms, a selection committee shall evaluate the responses and document the scoring and selection process	Responses received, scoring process and executed contract for professional services signed by the grantee

**If a single response is received,  
the grantee must draft a letter stating such**

# Formal Bidding

- For large projects; typically, construction related activities where an engineer or architect design plans and prepare formal bid documents (SPECS).
  - Once plans and SPECS are prepared and approved by TNECD and the Tennessee Historical Commission (THC) a bid date and location is set
- Bid opening must be advertised in a newspaper
  - Does not have to be daily
  - Consider other actions to solicit bidders
  - 14 days minimum between advertisement and bid opening
- Consider pre-bid meeting for complex projects
- All addenda must be approved by ECD
  - Submit at least 4 days prior to bid opening
  - State law requires 48 hours notice to bidders
- Must submit to the State's Go-BID website portal for construction
  - Decide who will submit. Typically submitted by the engineer.
- Think of ways to encourage participation from bidders
  - Utilize plans rooms
  - Industry networks (Dodge Report)
  - Keep a catalogue of potential bidders from previous project

# Construction Project Flowchart



# Formal Bidding for Construction

- All construction activities must be competitively bid following applicable state and local procurement laws
- See our [website](#) for our bidding procedures and fillable bid packet
- Bid packets must be approved prior to being advertised. Addendums must also be submitted for approval to allow for at least 48 hours notice to bidders
- Publicly open bids must be documented via bid opening minutes
- Once bids are received, certified bid tabs must also be approved

**Note: No contracts may be signed, and no work can be completed until after the grant contract with the State is executed**

# Construction Projects Continued

## Items that require approvals

- Plans & Specifications
- Addendums
- Certified (stamped) Bid tabs & Recommendation of Award
- Change Orders

## Additional documents needed by TNECD

- Professional services procurement documentation
- Copy of bid advertisement
- Notice of Award & pre-construction conference
- Notice to Proceed
- Closeout documents (Notice of Completion & Release of Liens)

# Informal Purchases

- Typically \$10,001 to \$50,000
- Purchases that fall under the threshold for formal bidding may use the informal purchase method
- At least (3) quotes must be included to show lowest prices was selected
- All quotes must be signed by the vendor

## *Example*

The grantee was awarded grant funds for large digital sign. The grantee contacted (3) sign vendors and received signed quotes from each one and selected the lowest cost sign.

**Subject to local thresholds**

# Micro Purchases

- Typically \$10,000 or less for goods; subject to local thresholds.
- At least (3) written quotes, such as screenshots from online shopping websites

## *Example*

The grantee was awarded grant funds to purchase supplies for a lab. They visited (3) websites to price beakers; took a screen shot of each website and selected the lowest cost beakers.

**Subject to local thresholds**

# Statewide Contract List

- List of active statewide contracts
- Check the usage instructions
- **Documentation to be Sent to ECD prior to purchase**
  - Letter of recommendation signed by the mayor on grantee letterhead (recommending award to the specified vendor)
  - Draft purchase order with detailed equipment costs and total
  - All required equipment vendor certifications signed by the selected vendor (found in Exhibit F-5 of the CDBG Manual)

# Cooperative Purchase

- Under T.C.A. § 12-3-1205 local governments are allowed to utilize cooperative purchases agreements with other governments inside or outside the state.
- **Step 1: Approval to Procurement**
  - Adopted resolution agreeing to the terms of the master agreement of the cooperative purchase service/platform
  - Proof that the CoOp/Platform is compliant with TCA Code (usually listed somewhere on the CoOp website)
  - A letter from the community explaining the equipment to be purchased and requesting to use the specified service/platform to procure the equipment
- **Step 2: Approval to Purchase**
  - Letter of recommendation signed by the mayor on grantee letterhead (recommending award to the specified equipment vendor)
  - Draft purchase order with detailed equipment costs and total
  - All required equipment vendor certifications signed by the selected vendor (found in Exhibit F-5 of the CDBG Manual)

# Sole Source

- May be allowed in very special circumstances
  - Single source of availability
  - Compatibility
- The selected vendor must still agree to sign all applicable certifications and affidavits.
- Inform your project manager if using this method.
- Vendor must document that they have sole source rights.
- Must be heavily documented in a memo provided to TNECD.
- Approval by TNECD before purchase.

# Invoicing

- Once you have received your executed contract, you will receive an invoice template that is specific to this grant
- Reimbursable grant - work must be completed and paid for by the grantee in order to submit a reimbursement request
- All back-up documentation must show dates of service and include a description of the services provided or work completed
- Each invoice must include proof of payment in the form of a copy of a canceled check, bank statement, or credit card statement
- The completed invoice template & all supporting documentation must be submitted to TNECD ([ecd.invoices@tn.gov](mailto:ecd.invoices@tn.gov)) for you to be reimbursed

# Eligible Expenses

- Any expenditure for a structural component of a building is eligible for grant funds. Treasury Regulation 1.48-1(e)(2) defines structural components to include
  - walls, partitions, floors, ceilings, permanent coverings such as paneling or tiling, windows and doors, components of central air conditioning or heating systems, plumbing and plumbing fixtures, electrical wiring and lighting fixtures, chimneys, stairs, escalators, elevators, sprinkling systems, fire escapes, and other components related to the operation or maintenance of the building.
- In addition to the above named "hard costs," there are "soft costs" which also qualify.
  - These include construction period interest and taxes, architect fees, engineering fees, construction management costs, reasonable developer fees, and any other fees paid that would normally be charged to a capital account. More information on soft costs can be found on the Technical Preservation Services website.
- Secretary of Interior Standards on Rehabilitation
- TNECD will work with the Tennessee Historical Commission (THC) on the NPS Part 1 and Part 2 that will be submitted as attachments with your application for compliance with the standards.
  - NPS Part 2 will become the scope of work for your grant contract. All work must be approved with this document; there are conditions from the THC on this document. Please read this document carefully.

# Reimbursement Requirements

- This is a **100% REIMBURSABLE grant**; you must have 100% of the project financing up front.
  - work **must** be completed in order to submit an invoice to the State at project closeout
- Project can be invoiced for 50% after monitoring by THC
- All back-up documentation for reimbursement **must** show dates of service and include a description of the service provided or work completed
- Expenses **must** be paid by contract grantee and proof of payment must be included in reimbursement request
- After grantees are selected, another webinar will be held to cover invoicing, compliance, etc.

# Requesting Reimbursement

## Completing the Invoice Template

**INVOICE REQUEST FOR PAYMENT**

<b>Grantee Name</b> Edison Address: I Edison Location: Man ECD SpeedStart# or Program#: 222700 Edison Contract ID#: 10345 ECD Department ID#: 220270000 Edison Vendor ID#: 54321 County: Davidson		<b>Invoice Request Number:</b> Final Invoice Request? YES or NO: Date of Invoice: Invoice Period: <span style="border: 1px solid black; padding: 2px;">Beginning</span> <span style="border: 1px solid black; padding: 2px;">End</span> Amount of this Request: 0.00	
<b>Remit To:</b> Grantee Remit Address:			

Budget Line-Item	Total Project	Grantee Participation	Grantee Participation %	Grant Budget	% Grant Funds	Amount of Grant Funds Previously Invoiced	Beginning Grant Balance	Amount Requested for Current Invoice Period	Cumulative Amount Invoiced	Ending Grant Balance	Cumulative Percent Invoiced
A. Construction	\$1,556,392.00	\$778,196.00	50.00%	\$778,196.00	50.00%	\$0.00	\$778,196.00	\$0.00	\$0.00	\$778,196.00	0.00%
B. Construction Inspection	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
C. Engineering Design	\$296,688.00	\$148,344.00	50.00%	\$148,344.00	50.00%	\$0.00	\$148,344.00	\$0.00	\$0.00	\$148,344.00	0.00%
D. Engineering (Other than design)	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
E. Legal Services	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
F. Appraisal	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
G. Acquisition of Property	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
H. Capital Purchase	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
I. Professional Fee	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
J. Project Contingency	\$205,000.00	\$102,500.00	50.00%	\$102,500.00	50.00%	\$0.00	\$102,500.00	\$0.00	\$0.00	\$102,500.00	0.00%
<b>Total</b>	<b>\$2,050,000.00</b>	<b>\$1,025,000.00</b>	<b>50.00%</b>	<b>\$1,025,000.00</b>	<b>50.00%</b>	<b>\$0.00</b>	<b>\$1,025,000.00</b>	<b>\$0.00</b>	<b>\$0.00</b>	<b>\$1,025,000.00</b>	<b>0.00%</b>

**With my signature, I certify the expenses requested for reimbursement were incurred:**  
 For the contract project area only, or middle mile infrastructure necessary to serve the contract project area; and  
 All contract procurement requirements were followed.

Authorized Signature: \_\_\_\_\_ Title: President Date: \_\_\_\_\_

**Please email your invoice including the first three tabs and backup documentation to [ECD.Invoices@tn.gov](mailto:ECD.Invoices@tn.gov)**

Grant Budget
Invoice
Backup Detail
Instructions
+



# Grant Budget Tab

Total Project Amount	\$50,000.00									
Grant Amount	\$50,000.00									
Percent of Grant Funds/Match Requirement (%)	100.00%									
Budget Line-Item	Initial Total Grant Budget	Revision 1/ Amendment	Revision 2/ Amendment	Revision 3/ Amendment	Revision 4/ Amendment	Revision 5/ Amendment	Revision 6/ Amendment	Revision 7/ Amendment	Current Project Budget	
A Salaries, Benefits & Taxes	\$0.00								\$0.00	
B Professional Fee, Grant & Award	\$50,000.00								\$50,000.00	
C Supplies, Telephone, Postage & Shipping,	\$0.00								\$0.00	
D Travel, Conferences & Meetings	\$0.00								\$0.00	
E Interest	\$0.00								\$0.00	
F Insurance	\$0.00								\$0.00	
G Specific Assistance to Individuals	\$0.00								\$0.00	
H Deprecitation	\$0.00								\$0.00	
I Other Non-Personnel	\$0.00								\$0.00	
J Capital Purchase	\$0.00								\$0.00	
K Indirect Cost	\$0.00								\$0.00	
L In-Kind Expense	\$0.00								\$0.00	
Total	\$50,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$50,000.00	

The Budget tab documents the original contract budget and any budget revisions that are made throughout the project.

If you revise the budget through TNECD, you'll get a new Invoice Template. We can't process any requests unless they are on the most up to date template.

# Backup Detail Tab

INVOICE REQUEST FOR PAYMENT						
Grantee Name			Invoice Request Number:		1	
Edison Address			Final Invoice Request? YES or NO? :		YES	
Edison Location			Date of Invoice:		10/20/20	
ECD Speedchart# or Program#:			Invoice Period:		Beginning: 10/01/20      End: 10/17/20	
Edison Contract ID# :			Amount of this Request:		30,000.00	
ECD Department ID#:			ECD Prog. Mgr., Title			
Edison Vendor ID#:			Grantee Contact Name			
County:			Email Address			
Remit To:			Phone number			
<b>Your organization's info</b>						
Budget Line-Item	Contractor	Contractor	Total	Amount of	Amount	
Payee/Vendor Name	Invoice	Invoice	Project	Grantee	Charged to	
	Number	Date	Amount	Participation	Grant Contract	
			Invoiced			
<b>Construction</b>				50.00%	50.00%	
A1 Example Construction	112	10/01/20	\$50,000.00	\$25,000.00	\$25,000.00	
A2				\$0.00	\$0.00	
A3				\$0.00	\$0.00	
A4				\$0.00	\$0.00	
A5				\$0.00	\$0.00	
A6				\$0.00	\$0.00	
A7				\$0.00	\$0.00	
A8				\$0.00	\$0.00	
A9				\$0.00	\$0.00	
A10				\$0.00	\$0.00	
Total Construction			\$50,000.00	\$25,000.00	\$25,000.00	
<b>Construction Inspection</b>				0.00%	0.00%	
B1				\$0.00	\$0.00	
B2				\$0.00	\$0.00	
B3				\$0.00	\$0.00	
B4				\$0.00	\$0.00	
B5				\$0.00	\$0.00	
B6				\$0.00	\$0.00	
B7				\$0.00	\$0.00	
B8				\$0.00	\$0.00	
B9				\$0.00	\$0.00	
B10				\$0.00	\$0.00	
Total Construction Inspection			\$0.00	\$0.00	\$0.00	
<b>Engineering Design</b>				50.00%	50.00%	
C1 Example Engineering	223	10/17/20	\$10,000.00	\$5,000.00	\$5,000.00	
C2				\$0.00	\$0.00	
C3				\$0.00	\$0.00	

This was established during contracting

The blue areas on this tab must be filled out and will automatically populate the invoice tab.

The totals will automatically calculate as you add lines in each budget section

The information for each vendor invoice you claim for reimbursement will need to be entered in the corresponding budget sections. In addition, the backup documents that contain the vendor invoices and proof of payment will need to be labeled, based on the line they are listed on in this tab (A1 C1, etc..).



# Backup Detail Tab Invoice Request Number

- Ensure to include the sequential number of grantee's project's invoice requests submitted to ECD.
- For example, it will be 1 if this is the first request.

Invoice Request Number:	5
Final Invoice Request? YES or NO?:	NO
Date of Invoice:	10/03/24

This number indicates that this is **the 5th reimbursement request package submitted by the project to ECD**, not counting revised versions, and it should not include any other information.

# Backup Detail Tab

## Determining Invoice Period

- The invoice period on the backup detail tab needs to be filled out based on the earliest and the latest **service dates** represented in the invoices included in the reimbursement request.
- Include service dates from the same fiscal year in a request, which runs from July 1 to June 30.

	Beginning	End
Invoice Period:	04/01/25	06/04/25

OSBORNE CONSTRUCTION

Invoice No. 18764

Date: May 30, 2025

Service period **April 1** - 30, 2025



BROWN ELECTRIC

Invoice No. 33365

Date: June 11, 2025

Service period April 30 through May 31, 2025

**Hickman Contractors, LLC**

Invoice No. 45796

Date: June 5, 2025

Service period May 5, 2025, through **June 4**, 2025

# Backup Detail Tab Budget Line Items

- Each line entered on the backup detail tab should represent 1 individual receipt/vendor invoice.


Budget Line-Item	Contractor	Contractor	Total Project	Amount of	Amount
Payee/Vendor Name	Invoice	Invoice	Amount	Grantee	Charged to
	Number	Date	Invoiced	Participation	Grant Contract
<b>Construction</b>				25.00%	75.00%
A1 ABC Construction (123 Example Sq)	123	10/20/21	\$2,500.00	\$624.98	\$1,875.02
A2 ABC Window (123 Example Sq)	1234	09/03/21	\$725.00	\$181.24	\$543.76
A3 ABC Building Supply (123 Example Sq)	12345	07/01/21	\$108.29	\$27.07	\$81.22
Δ1				\$0.00	\$0.00

# Backup Detail Tab

## Contractor Invoice Number

Budget Line-Item	Contractor	Contractor
Payee/Vendor Name	Invoice	Invoice
	Number	Date
<b>Construction</b>		
A1 Osborne Construction	18764	05/30/25
A2 Hickman Contractors, LLC	45796	06/05/25
A3 Brown Electric	33365	06/11/25

- The contractor invoice number can be found on the vendor invoice/ supporting documentation

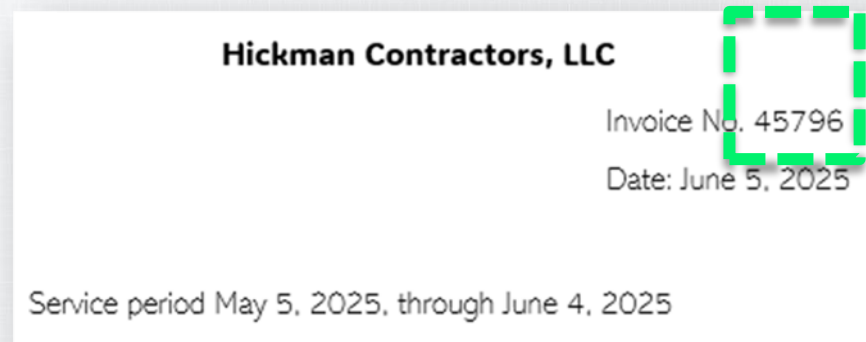

# Backup Detail Tab Contractor Invoice Date

Budget Line-Item	Contractor	Contractor
Payee/Vendor Name	Invoice Number	Invoice Date
<b>Construction</b>		
A1 Osborne Construction	18764	05/30/25
A2 Hickman Contractors, LLC	45796	06/05/25
A3 Brown Electric	33365	06/11/25

**Hickman Contractors, LLC**

Invoice No. 45796  
Date: June 5, 2025

Service period May 5, 2025, through June 4, 2025

# Labeling and Proof of Payment

- Each receipt/vendor invoice must have proof of payment. TNECD accepts copies of the cancelled check, bank/credit card statements, or a detailed check stub.
- Each vendor invoice needs to be labeled to connect it back to the appropriate line item in the backup detail tab

Budget Line-Item
Payee/Vendor Name
<b>Construction</b>
A1 Osborne Construction
A2 Brown Electric
A3 Hickman Contractors, LLC

**A1**

OSBORNE CONSTRUCTION Invoice No. 18764  
Date: May 30, 2025

Service period April 1 – 30, 2025

**A2**


 BROWN ELECTRIC Invoice No. 33365  
Date: June 11, 2025

Service period April 30 through May 31, 2025

**A3**

Hickman Contractors, LLC Invoice No. 45796  
Date: June 5, 2025

Service period May 5, 2025, through June 4, 2025



# Quality Invoices

Engineering Services through 02-02-25

50% of Lump Sum Amount of \$114,000.00

\$57,000.00

**TOTAL AMOUNT DUE THIS STATEMENT**

**\$57,000.00**

For Professional Services Rendered Through 3/28/2025

	Fee	% Complete	Billings		
			To Date	Previous	Current
1000 - Survey & GIS Development	162,000.00	40.00	64,800.00	40,354.20	24,445.80
2000 - Water Distribution System Modeling	156,000.00	3.00	4,680.00	0.00	4,680.00
3000 - Wastewater System Modeling	180,000.00	0.00	0.00	0.00	0.00
<b>Current Billings</b>					<u>29,125.80</u>
<b>Amount Due This Bill</b>					<u><u>29,125.80</u></u>

For services performed 04/01/25 - 04/30/25

Description	Contract Amount	Percent Complete	Prior Billed	Total Billed	Current Billed
<b>System Investigation</b>	185,000.00	2.84	0.00	5,250.00	5,250.00
<b>Infiltration and Inflow Reduction and Elimination Plan</b>	15,000.00	0.00	0.00	0.00	0.00
<b>Total</b>	200,000.00	2.63	0.00	5,250.00	5,250.00

*Signatures* Invoice total

**5,250.00**



# Invoice Tab

**INVOICE REQUEST FOR PAYMENT**

<b>Grantee Name</b>	
Edison Address	I
Edison Location	Main
ECD Speedchar# or Program#	330790
Edison Contract ID#	12045
ECD Department ID#	3300700100
Edison Vendor ID#	54321
County	Davidson
Remit To:	
Grantee Remit Address	

Invoice Request Number:   
 Final Invoice Request? YES or NO?:   
 Date of Invoice:   
 Invoice Period: 

Beginning	End
-----------	-----

  
 Amount of this Request:

This column will need to be filled out based on your previous requests, starting with reimbursement request two.

These will be auto populated from the Backup Detail tab

Budget Line-Item	Total Project	Grantee Participation	% Grantee Participation	Grant Budget	% Grant Funds	Amount of Grant Funds Previously Invoiced	(Beginning Grant Balance	Amount Requested for Current Invoice Period	Cumulative Amount Invoiced	Ending Grant Balance	Cumulative Percent Invoiced
A Construction	\$1,558,352.00	\$779,856.00	50.00%	\$779,856.00	50.00%	\$0.00	\$779,856.00	\$0.00	\$0.00	\$779,856.00	0.00%
B Construction Inspection	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
C Engineering Design	\$286,688.00	\$143,344.00	50.00%	\$143,344.00	50.00%	\$0.00	\$143,344.00	\$0.00	\$0.00	\$143,344.00	0.00%
D Engineering (Other than design)	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
E Legal Services	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
F Appraisals	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
G Acquisition of Property	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
H Capital Purchase	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
I Professional Fee	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
J Project Contingency	\$205,000.00	\$102,500.00	50.00%	\$102,500.00	50.00%	\$0.00	\$102,500.00	\$0.00	\$0.00	\$102,500.00	0.00%
<b>Total</b>	<b>\$2,050,000.00</b>	<b>\$1,025,000.00</b>	<b>50.00%</b>	<b>\$1,025,000.00</b>	<b>50.00%</b>	<b>\$0.00</b>	<b>\$1,025,000.00</b>	<b>\$0.00</b>	<b>\$0.00</b>	<b>\$1,025,000.00</b>	<b>0.00%</b>

**With my signature, I certify the expenses requested for reimbursement were incurred:**  
 For the contract project area only, or middle mile infrastructure necessary to serve the contract project area; and  
 All contracted procurement requirements were followed.

Authorized Signature:

Title:

Date:

A signature and date are required in order to process the request. We do not accept typed signatures. It must be a wet signature or digitally verified.

**Please email your invoice including the first three tabs and backup documentation to [ECD.Invoices@tn.gov](mailto:ECD.Invoices@tn.gov)**

Grant Budget
Invoice
Backup Detail
Instructions



# Invoice Template

## Amount of Grant Funds Previously Invoiced

Remit To:

P.O. Box 368  
Pulaski, TN 38478

Invoice Request Number: 33  
(What Invoice Request? Year or No?)

Date of Invoice: 06/17/24

Invoice Period	Beginning	End
	07/08/24	07/31/24

Contract Period	Begin Date	End Date
	09/06/22	08/31/25

Amount of this Request: \$2,457.53

ECD Contact: Taylor Bealy, Broadband Director

Budget Line-Item	Total Project	Grantee Participation	% Grantee Participation	Grant Budget	% Grant Funds	Amount of Grant Funds Previously Invoiced	Beginning Grant Balance	Amount Requested for Current Invoice Period	Cumulative Amount Invoiced	Ending Grant Balance	Cumulative Percent Invoiced
A. Construction (including inspection)	\$27,894,199.14	\$8,368,259.74	30.00%	\$19,525,939.40	70.00%	\$12,579,986.39	\$6,945,963.01	\$309,867.53	\$12,889,853.92	\$6,285.48	66.01%
B. Engineering and Design	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
C. Legal Services	\$194,178.57	\$58,253.57	30.00%	\$135,925.00	70.00%	\$0.00	\$350.00	\$350.00	\$350.00	\$3,575.00	2.26%
D. Appraisals	\$109,706.47	\$32,911.94	30.00%	\$76,794.53	70.00%	\$0.00	\$76,794.53	\$0.00	\$0.00	\$76,794.53	0.00%
E. Acquisition of Property	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
F. Capital Purchase	\$513,022.28	\$153,906.68	30.00%	\$359,115.60	70.00%	\$14,325.60	\$209,790.00	\$132,790.00	\$282,115.60	\$7,000.00	78.56%
G. Project Contingency	\$4,376,948.57	\$1,313,084.57	30.00%	\$3,063,864.00	70.00%	\$0.00	\$3,063,864.00	\$0.00	\$0.00	\$3,063,864.00	0.00%
<b>Total</b>	<b>\$33,088,055.03</b>	<b>\$9,926,416.50</b>	<b>30.00%</b>	<b>\$23,161,638.53</b>	<b>70.00%</b>	<b>\$12,739,991.99</b>	<b>\$10,431,976.54</b>	<b>\$442,457.53</b>	<b>\$13,172,119.52</b>	<b>\$9,989,519.01</b>	<b>56.87%</b>

Remit To:

P.O. Box 368  
Pulaski, TN 38478

Invoice Request Number: 34  
(What Invoice Request? Year or No?)

Date of Invoice: 10/03/24

Invoice Period	Beginning	End
	07/01/24	08/31/24

Contract Period	Begin Date	End Date
	08/05/22	08/31/25

Amount of this Request: \$60,446.66

ECD Contact: Taylor Bealy, Broadband Director

Budget Line-Item	Total Project	Grantee Participation	% Grantee Participation	Grant Budget	% Grant Funds	Amount of Grant Funds Previously Invoiced	Beginning Grant Balance	Amount Requested for Current Invoice Period	Cumulative Amount Invoiced	Ending Grant Balance	Cumulative Percent Invoiced
A. Construction (including inspection)	\$27,894,199.14	\$8,368,259.74	30.00%	\$19,525,939.40	70.00%	\$12,889,853.92	\$6,536,285.48	\$550,446.56	\$13,440,100.48	\$5,795,838.92	70.31%
B. Engineering and Design	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
C. Legal Services	\$194,178.57	\$58,253.57	30.00%	\$135,925.00	70.00%	\$350.00	\$350.00	\$350.00	\$350.00	\$3,575.00	2.26%
D. Appraisals	\$109,706.47	\$32,911.94	30.00%	\$76,794.53	70.00%	\$0.00	\$76,794.53	\$0.00	\$0.00	\$76,794.53	0.00%
E. Acquisition of Property	\$0.00	\$0.00	0.00%	\$0.00	0.00%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
F. Capital Purchase	\$513,022.28	\$153,906.68	30.00%	\$359,115.60	70.00%	\$282,115.60	\$77,000.00	\$0.00	\$282,115.60	\$7,000.00	78.56%
G. Project Contingency	\$4,376,948.57	\$1,313,084.57	30.00%	\$3,063,864.00	70.00%	\$0.00	\$3,063,864.00	\$0.00	\$0.00	\$3,063,864.00	0.00%
<b>Total</b>	<b>\$33,088,055.03</b>	<b>\$9,926,416.50</b>	<b>30.00%</b>	<b>\$23,161,638.53</b>	<b>70.00%</b>	<b>\$13,172,119.52</b>	<b>\$9,989,519.01</b>	<b>\$60,446.66</b>	<b>\$14,027,966.08</b>	<b>\$9,139,072.45</b>	<b>60.54%</b>




# Helpful Tips

## Based on Common Mistakes

- When you are ready to submit the request combine your signed invoice coversheet, all backup detail pages, and backup documentation into **ONE** pdf document.
- The request should be in order and there should be handwritten/typed labels on each page of the document to tie it back to the backup detail lines.
- Information for all applicable fields must be completed on the invoice template and the coversheet must be signed and dated prior to submission.
  - **Please don't forget to double check that the "Amount of Grant Funds Previously Invoiced" column has been updated prior to signing the coversheet.**
- Submit invoices no more than monthly and no less than quarterly to [ecd.invoices@tn.gov](mailto:ecd.invoices@tn.gov)

# Payment Timeline

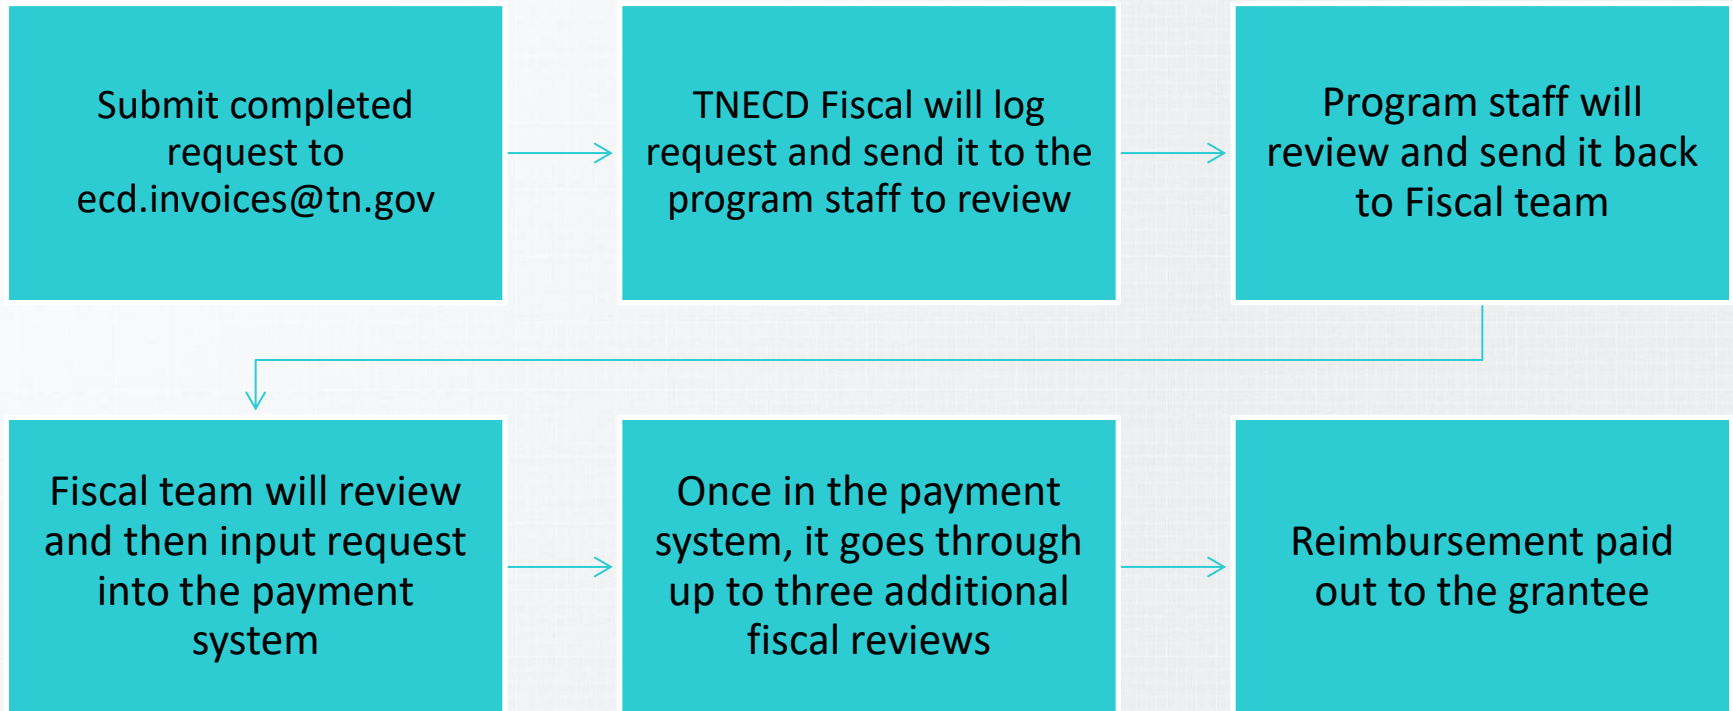

*Please allow at least 4-5 weeks for processing invoices from submission date. If changes are required between the program staff review and/or fiscal staff review this estimated timeline starts over.*

# Reporting

- Annual Reports – Due each year on the contract anniversary date
- Monthly Reports – Due on the 25<sup>th</sup> of every month

 <b>GOVERNMENTAL GRANT CONTRACT</b> (cost reimbursement grant contract with a federal or Tennessee local governmental entity or their agents and instrumentalities)			
<b>Begin Date</b> You cannot incur expenses before this date	<b>End Date</b> You cannot incur expenses after this date	<b>Agency Tracking #</b> The number of the program internally (budget)	<b>Edison ID</b> The number for this contract, also referred to as a "PO" number
<b>Grantee Legal Entity Name</b> Legal Name of your organization, including a dba, if applicable			<b>Edison Vendor ID</b> The number associated with your entity
<b>Subrecipient or Contractor</b> <input checked="" type="checkbox"/> Subrecipient <input type="checkbox"/> Contractor	<b>CFDA #</b> Grantee's fiscal year end This is the end of your fiscal year per your application and <del>pregrant</del>		

# Monitoring

- TNECD will be initiate monitoring once the project exceeds 50% completion. These may be on site and will be conducted by representatives from the Tennessee Historical Commission and TNECD.
- The main focus of the monitoring is to ensure that you did what you said you were going to do and what the contract said you were going to do, that you followed procurement policies, and that you have good records. Also, that you followed the conditions in Part 2.
- TNECD will review timeliness of quarterly and annual progress reporting to determine reporting compliance.

# Files

- Can keep files electronically or in hard copy
- **Basic Recommended File System:**
  - Application File
  - Contract file
  - Procurement
  - Financial Management
  - State Monitoring
  - Reporting
  - Closeout
- Keep files for 5 years after the close of the contract

# Closeout Documents

- A completed Part 3 form, as well as interior and exterior photographs keyed to a basic floorplan or sketch, sent to the TN Historic Commission for review and approval. Photos must be within a pdf, 2 per page, and include a short description of what is being viewed for context. This can be submitted to [thc.rehab@tn.gov](mailto:thc.rehab@tn.gov)
- Certificate of Occupancy
- Completed Reimbursement Request Submission
  - Final reimbursement request or request for payment (RFP) needs to be submitted within 30 days of contract end date to [ECD.Invoices@tn.gov](mailto:ECD.Invoices@tn.gov)
  - No invoices should be dated past the contract end date
  - All necessary reports should have been submitted before final RFP
- Closeout Report- The closeout report is to be submitted.
- All the above items must be received for us to process your final reimbursement request submission.

# Other Requirements

- We want your success stories! Take pictures! Let us know how this helps you understand your systems, apply for other funds, prevent problems, etc.
- Think about outcomes throughout the project
- All documents must be submitted electronically. Recommended Subject line for emails: Grantee-HDGP-Edison Contract ID#- Subject of email.
- Projects must be completed within the contract period – but you can definitely finish sooner
- It is important that you ask when you have questions as soon as they arise, rather than waiting until too late
- Technical Assistance Calls will be setup very soon with representatives from the Tennessee Historical Commission and TNECD to discuss your project in depth and go over your Part 2 and Conditions.
- Periodically review this presentation

# Contact Information

## TNECD

**Kim Parks – Tennessee Main Street Director-TNECD**  
[Kim.Parks@tn.gov](mailto:Kim.Parks@tn.gov)

**Frank Clark, TN Main Street Assistant Director**  
[frank.clark@tn.gov](mailto:frank.clark@tn.gov)

**Sarah Elizabeth Hickman-McLeod – Rural  
Development Grant Program Manager-TNECD**  
[sarah.hickman-mcleod@tn.gov](mailto:sarah.hickman-mcleod@tn.gov)

## Tennessee Historical Commission

**Lane Tillner-Technical Preservation Coordinator-  
CLG East Tennessee (Morgan, Pickett, Polk, and  
Scott)**  
[lane.tillner@tn.gov](mailto:lane.tillner@tn.gov)

**Stevie Malenowski-Technical Preservation  
Coordinator-CLG West Tennessee (Chester, Dickson,  
Giles, Lauderdale, Lawrence, Maury, and Weakley)**  
[Stevie.Malenowski@tn.gov](mailto:Stevie.Malenowski@tn.gov)

**Justin Heskew- Historic Preservation Supervisor &  
Federal Historic Tax Credits (Copy)**  
[Justin.Heskew@tn.gov](mailto:Justin.Heskew@tn.gov)

[Historic Development Grant TNECD Website](#)





QUESTIONS?
